




- LEGEND**
- Buildings (this contract)
 - ▨ External yards / hardstanding
 - /// Blasting zone — eastern third
 - - - Made ground (extent unproven)
 - 110 kV overhead line


- NOTES**
- Setting-out grid: numbered gridlines 1-24 at 18 m centres east-west; lettered gridlines A-J at 12 m centres north-south.
 - Bedrock at 4-8 m below existing ground. Blasting is required in the eastern third of the plot (hatched) — refer PDC-SS-001.
 - Area of unrecorded made ground in the north-west corner: approx. 900 m². Archaeological watching brief may be required.
 - No crane operation within the exclusion zone of the 110 kV overhead line without the network operator's written permission.
 - Night-time noise limit 45 dB(A) at the north-west residential boundary. Generator testing 09:00-16:00 weekdays only.
 - Site access from Tikurilaentie only, shared with an operating logistics neighbour. Deliveries 06:00-22:00 weekdays.

SITE DATA	
PLOT	92-52-7-2, AVIAPOLIS, VANTAA
PLOT AREA	48,300 m ² (4.83 ha)
BUILDING FOOTPRINT	12,837 m ²
SITE COVERAGE	26.6 %
TOTAL GFA	14,450 m ²
IT LOAD	10 MW (4 x 2.5 MW)
SITE CONNECTION	16 MVA, 110/20 kV
STANDBY GENERATION	8 x 2.5 MVA
SECTION 1 / 2 / 3 / 4	MONTH 14 / 16 / 19 / 22

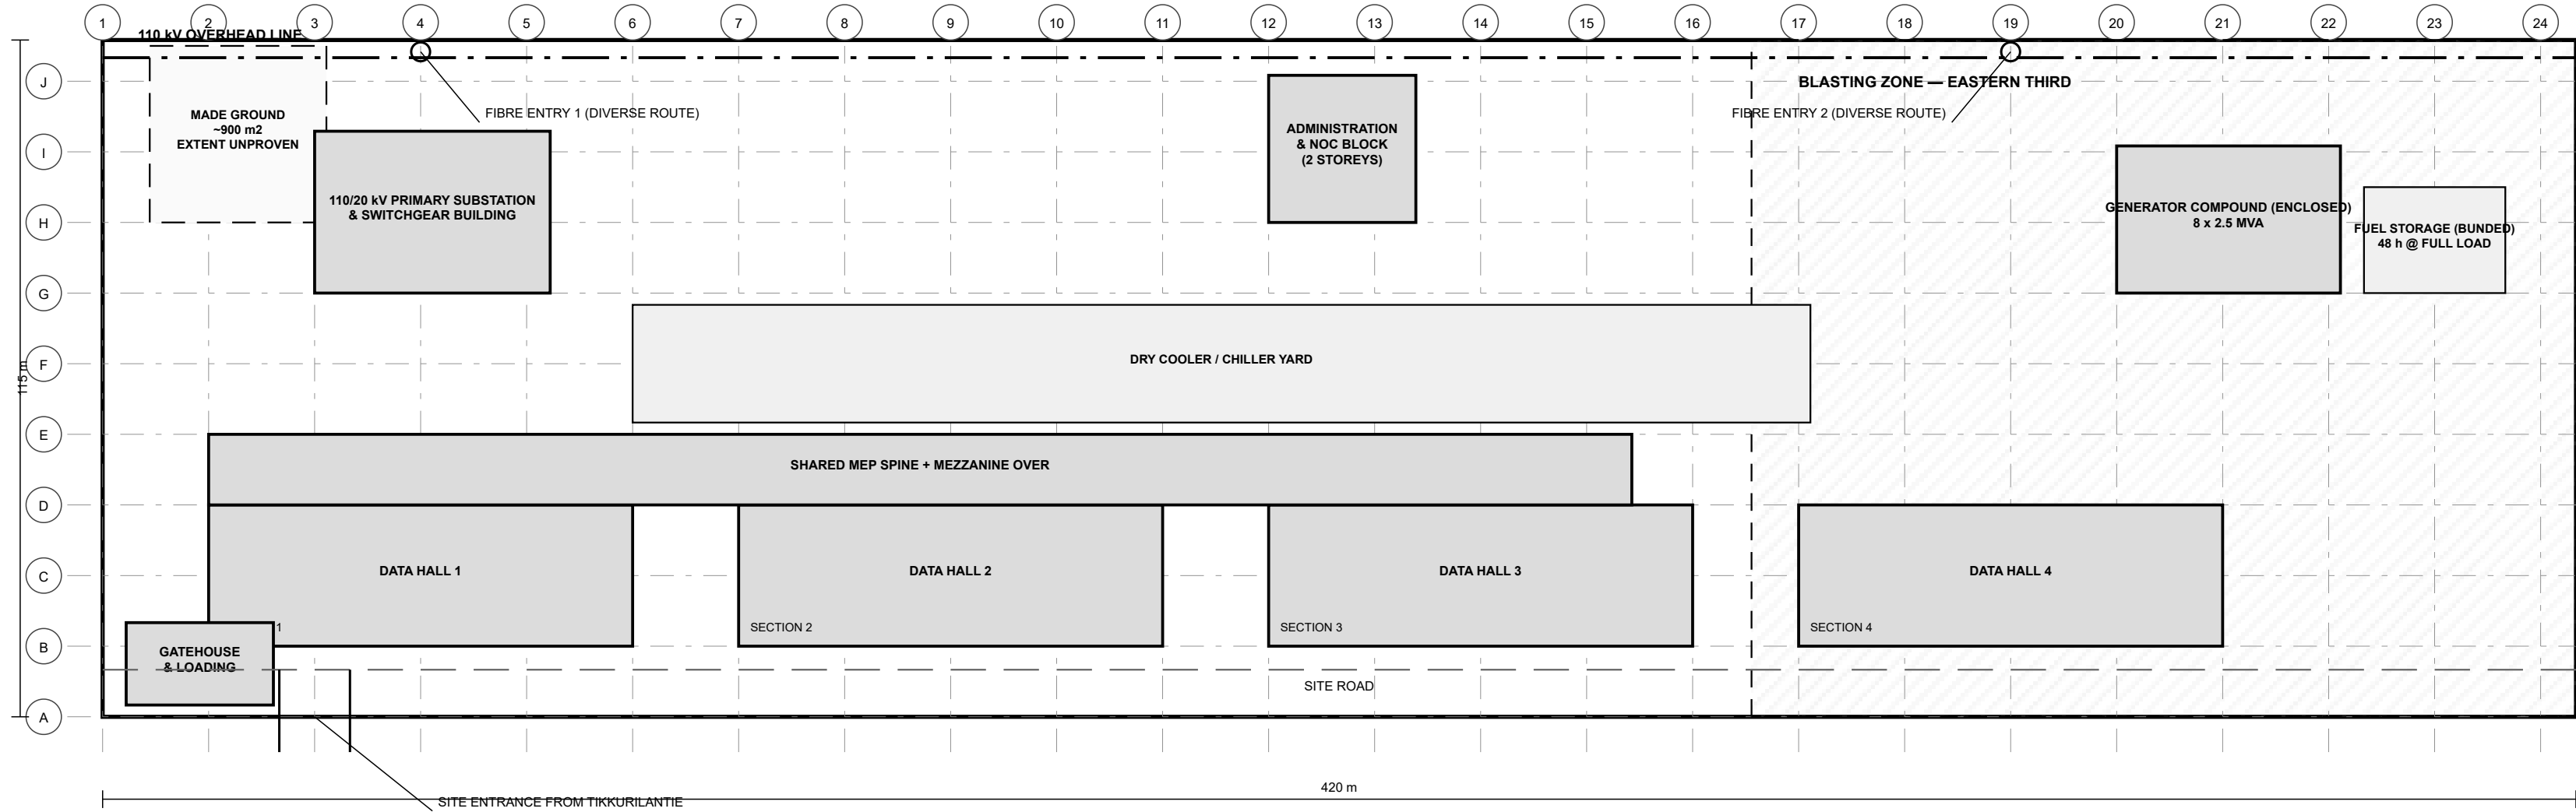

SECTIONAL COMPLETION — CONSTRUCTION SEQUENCE		
SECTION	SCOPE	COMPLETION
1	HALL 1 + SUBSTATION + GENERATORS + SHARED SPINE (FULL 10 MW) + ACCESS	MONTH 14
2	HALL 2 + ASSOCIATED PLANT	MONTH 16
3	HALL 3 + ASSOCIATED PLANT	MONTH 19
4	HALL 4 + ADMIN/NOC BLOCK + EXTERNAL WORKS	MONTH 22

Later Sections are constructed without re-entering the footprint of an operating Section. Halls are separated by one clear 18 m structural bay.



PROJECT POLARIS DC-1 — AVIAPOLIS DATA CAMPUS, PHASE... EMPLOYER POLARIS DIGITAL INFRASTRUCTURE OY CONTRACTOR NORDBUILD OY DRAWING SITE PLAN DISCIPLINE ARCHITECTURAL			
DWG No PDC-DWG-001 SYNTHETIC DEMONSTRATION DATA — NOT A REAL PROJECT	REV A	DATE 24.02.2026	SCALE 1:1000
