





- LEGEND**
- Column, plan (base below — see PDC-DWG-010)
  - Primary frame / roof truss centreline
  - Ridge tie beam
  - Roof wind bracing, end bays
  - Gable end post
  - Precast wall panel joint, 2.4 m module

- NOTES**
- Typical for Data Halls 1 to 4. Primary structure: steel braced-portal frame on the 18 m span, columns at 12 m centres — refer PDC-BOD-001 Section 4.1. Halls are clear-span in the 24 m direction; no internal columns within the white space.
  - Roof bracing bays are located at the end bays only, adjacent to each fire-compartment wall, so that no bracing bay crosses a compartment line.
  - Underside of primary steel at 6.6 m above finished floor level, coordinating a 2.4 m overhead service zone to achieve 4.2 m minimum clear height in white space — refer PDC-BOD-001 Section 3.2.
  - Column bases: refer PDC-DWG-010 for foundation type, size and bearing pressure at each grid intersection.
  - Precast concrete wall panels form the envelope and the EI 120 fire-separating walls between halls, continuous from foundation to underside of roof deck — refer PDC-BOD-001 Section 3.4.

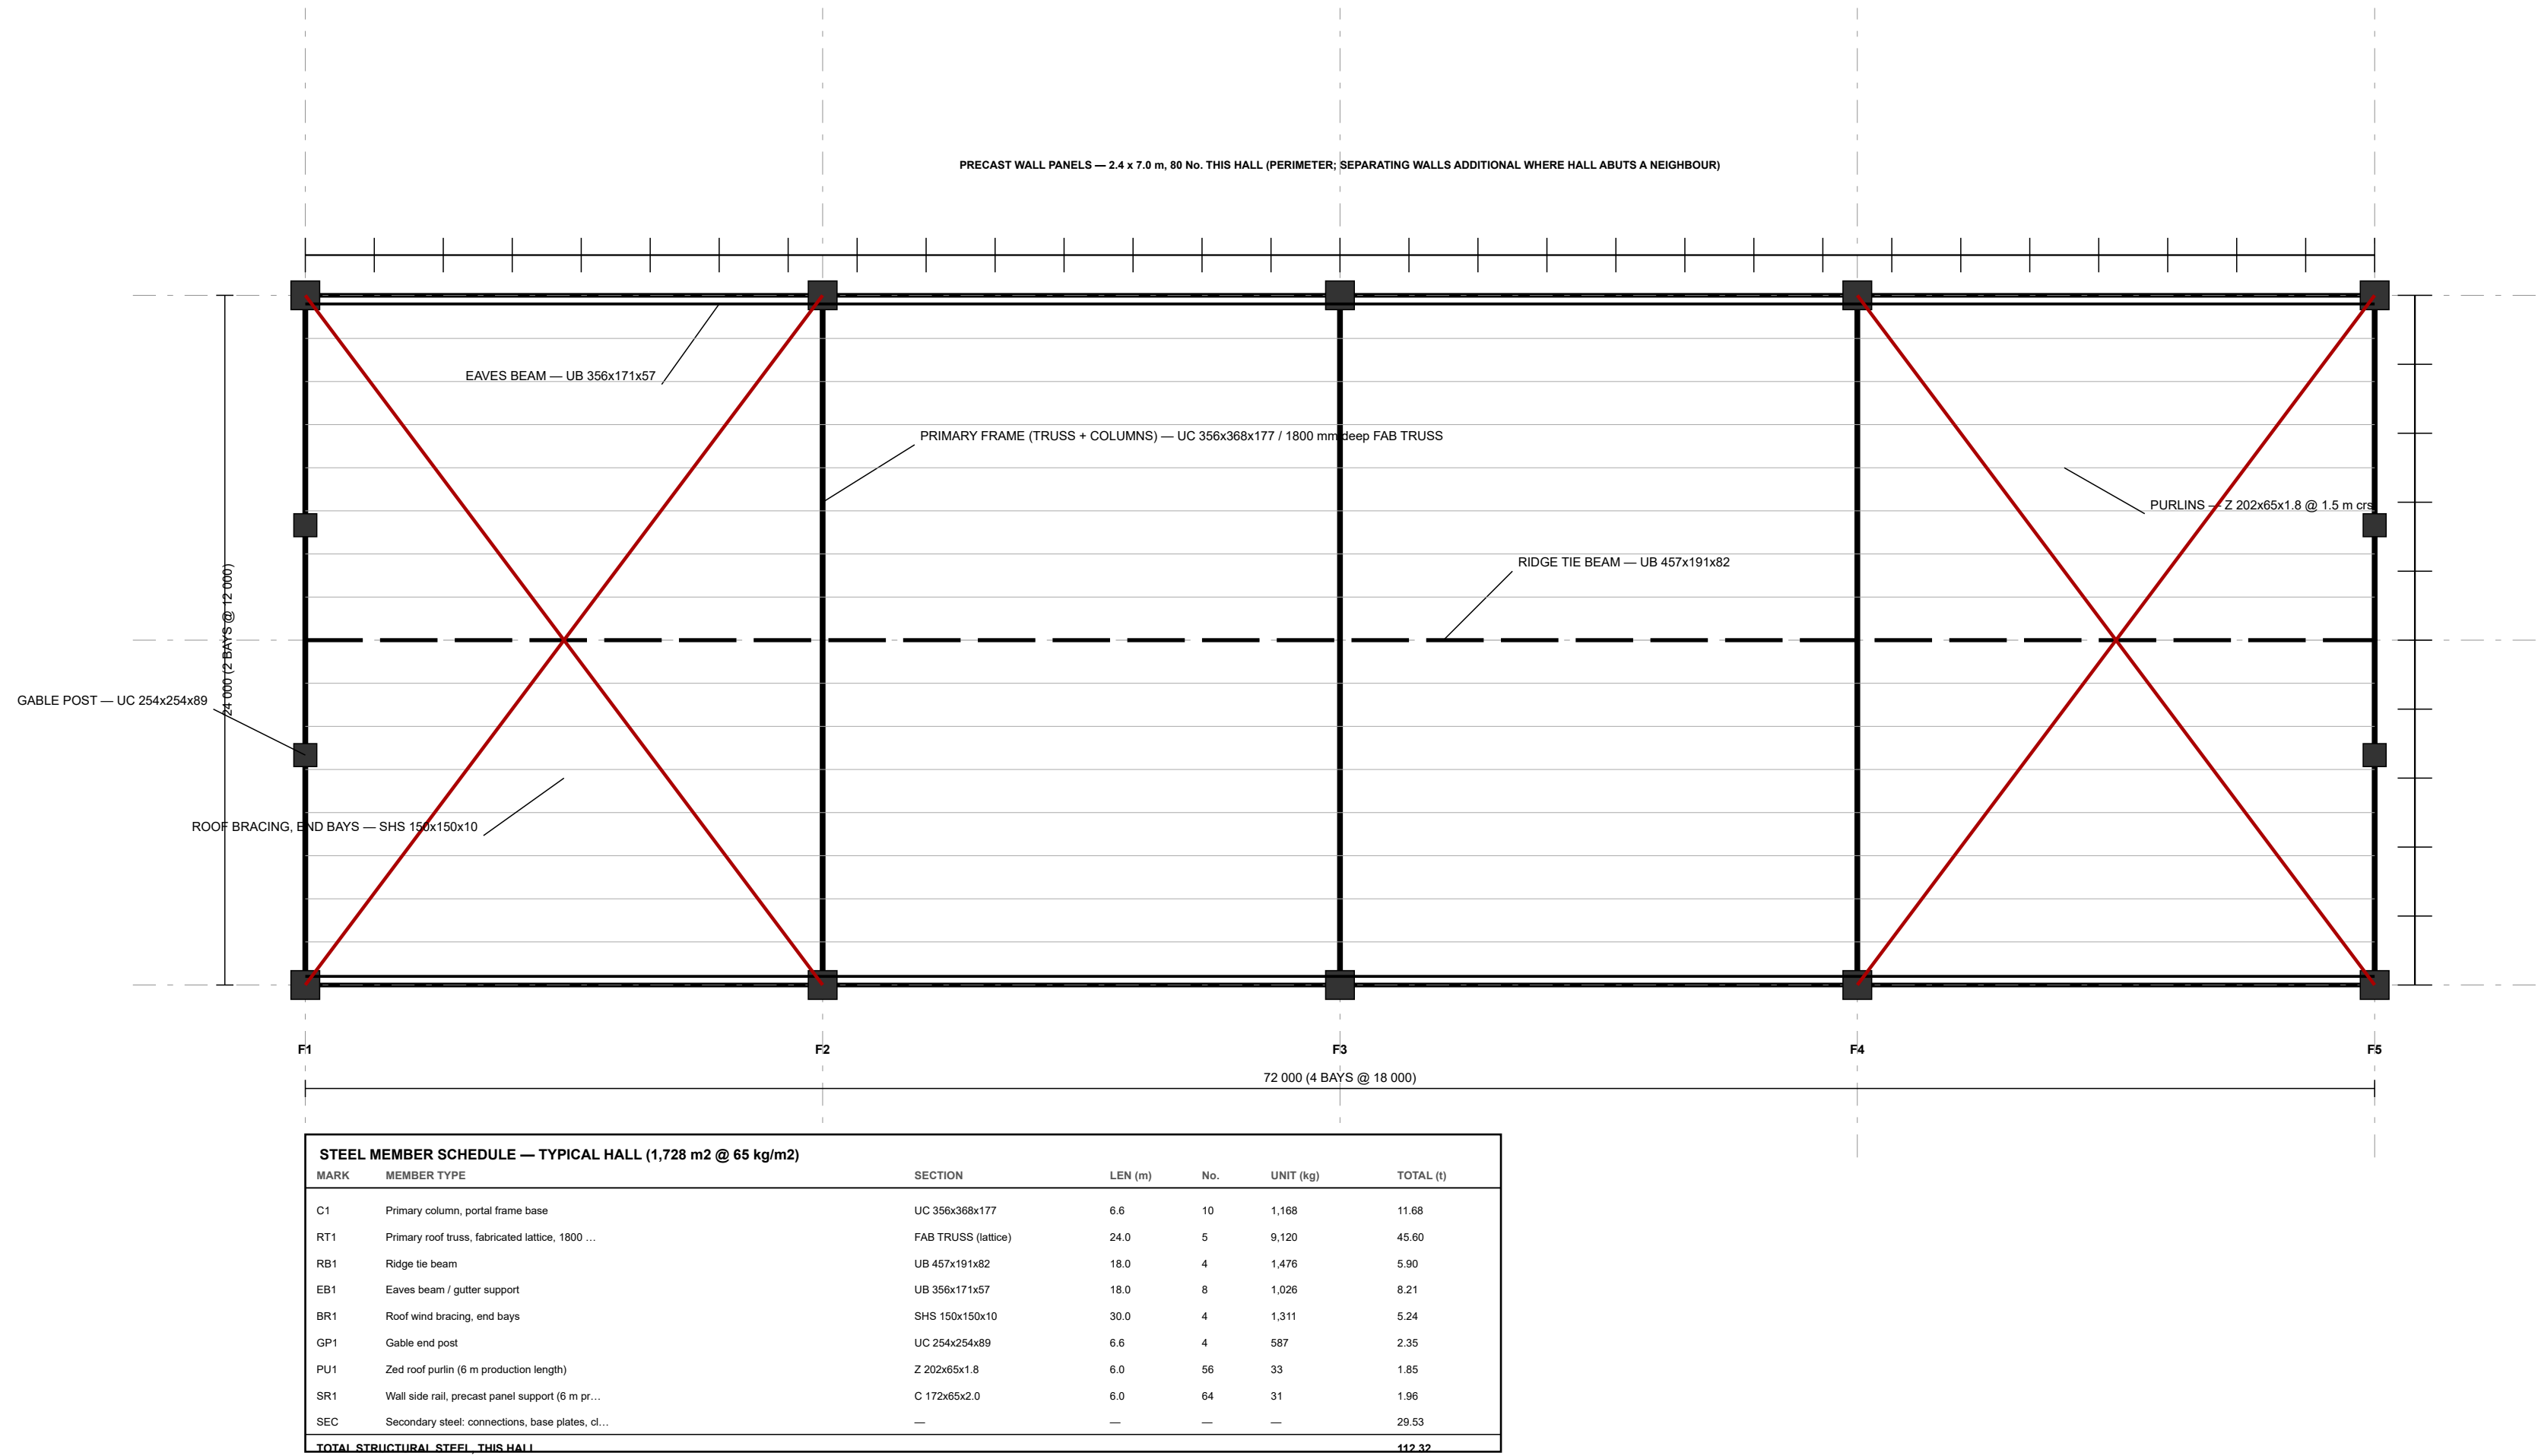

PROJECT  
**POLARIS DC-1 — AVIAPOLIS DATA CAMPUS, PHASE...**

EMPLOYER  
**POLARIS DIGITAL INFRASTRUCTURE OY**

CONTRACTOR  
**NORDBUILD OY**

DRAWING  
**STEEL FRAMING PLAN — TYPICAL DATA HALL**

DISCIPLINE  
**STRUCTURAL**

|                                                                                                  |                 |                           |                       |
|--------------------------------------------------------------------------------------------------|-----------------|---------------------------|-----------------------|
| DWG No<br><b>PDC-DWG-011</b><br><small>SYNTHETIC DEMONSTRATION DATA — NOT A REAL PROJECT</small> | REV<br><b>A</b> | DATE<br><b>24.02.2026</b> | SCALE<br><b>1:200</b> |
|--------------------------------------------------------------------------------------------------|-----------------|---------------------------|-----------------------|
