





- LEGEND**
- F1 Pad on till
 - F2 Enlarged pad, till near rockhead
 - F3 Pad, direct-to-rock
 - F4 Rock-socketed pier
 - Ground beam, typ
 - /// Blasting zone — eastern third
 - W Boulder horizon — rock level unproven
 - Made ground — not suitable for founding

- NOTES**
- Bedrock at 4-9 m below existing ground level, shallowest in the east (BH-05, BH-09, BH-13, BH-14) — refer PDC-SS-001 Section 3.1. Foundation type follows this gradient: pads on till in the west, transitioning to direct-to-rock and rock-socketed piers in the east.
 - Controlled blasting is required within the blasting zone (eastern third of the plot) to achieve founding levels — refer PDC-SS-001 Section 5 for repeatability, PPV vibration limits and neighbour notification.
 - Boulder-rich horizon of unproven extent between BH-07 and BH-08 (refusal on obstruction) and BH-09 (rock proven, boulders above) — rock level is NOT proven in this zone. Confirm founding level hole-by-hole; further investigation recommended ahead of piling — refer PDC-SS-001 Section 7a.
 - Made ground in the north-west corner, approx. 900 m2, extent and depth unproven — not suitable for direct founding. Remove and replace, or a piled slab solution, pending confirmation of fill extent — refer PDC-SS-001 Section 7b. A watching brief for archaeological potential may be required.
 - Ground-bearing slab: 25 kN/m2 uniform imposed load. PM2 fitness class throughout while space and support areas, no raised floor — refer PDC-BOD-001 Section 4.3.
 - Perched groundwater recorded at 2.6-3.9 m below existing ground level, seasonal variation 0.5-1.0 m expected. Allow sump pumping / well-pointing for excavations below approx. 2.5 m — refer PDC-SS-001 Section 4.

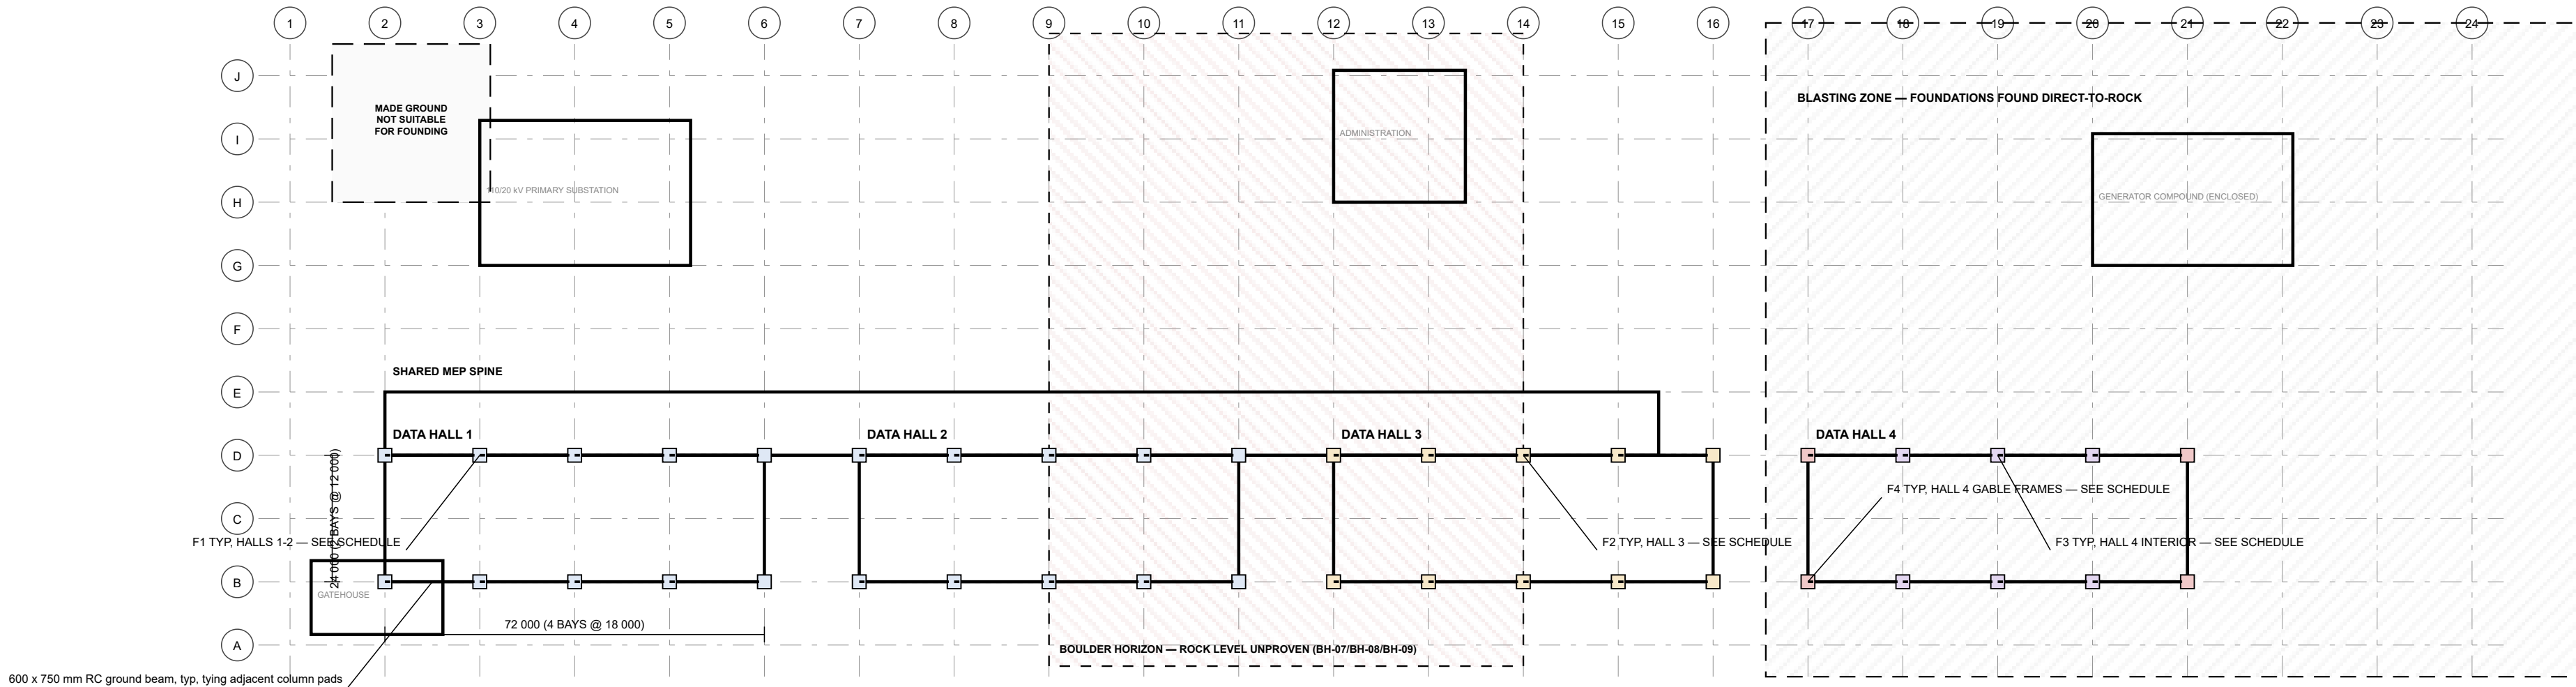

FOUNDATION SCHEDULE					
TYPE	SIZE	DEPTH	BEARING STRATUM	ALLOW. BEARING	No.
F1	2000x2000x600 pad	1.5 m	Compacted fill	250 kPa	20
F2	2600x2600x700 enlarged pad	3.0 m	Very stiff silt, near rockhead	325 kPa	10
F3	1800x1800x500 pad	0.5 m	Sound rock, direct bearing	2,500 kPa	6
F4	0.9 m dia rock-socketed pier	2.0 m socket	Sound rock, socketed pier	2,500 kPa	4
TOTAL FOUNDATIONS, 4 HALLS					40



PROJECT POLARIS DC-1 — AVIAPOLIS DATA CAMPUS, PHASE... EMPLOYER POLARIS DIGITAL INFRASTRUCTURE OY CONTRACTOR NORDBUILD OY DRAWING FOUNDATION PLAN — DATA HALLS 1-4 DISCIPLINE STRUCTURAL			
DWG No	REV	DATE	SCALE
PDC-DWG-010	A	24.02.2026	1:1000
SYNTHETIC DEMONSTRATION DATA — NOT A REAL PROJECT			
